


**TOWN OF TWISP - SECOND AVENUE IMPROVEMENTS  
CONSTRUCTION UPDATE AS OF SEPTEMBER 9, 2008**

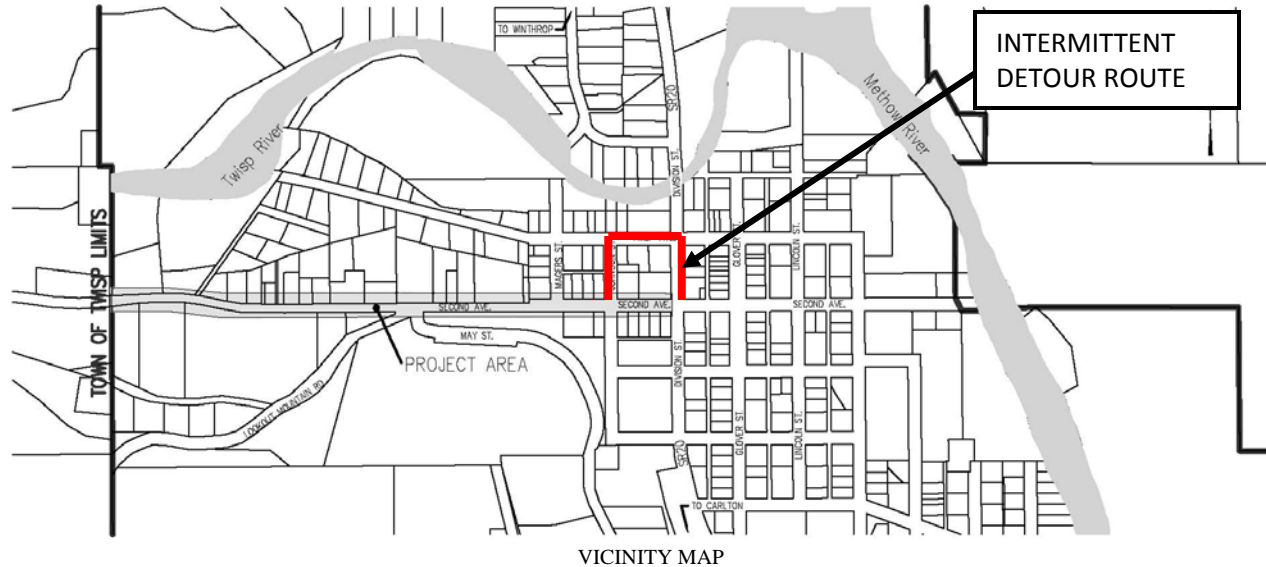

CONSTRUCTION IS CONTINUING ON SECOND AVENUE ...

- CONTRACTOR HAS COMPLETED ROUGH GRADING OF THE ROADWAY.
- CONTRACTOR HAS COMPLETED WATER MAIN TIE-INS AND SERVICE CONNECTIONS.
- CONTRACTOR HAS COMPLETED STORMWATER STRUCTURES.
- CONTRACTOR HAS COMPLETED MOST CURB AND GUTTER.
- FINAL SUBGRADE SURFACING – SEPTEMBER 10 - 14. (Weekend work is expected.)
- PAVING IS SCHEDULED FOR THE WEEK OF SEPTEMBER 15!!! (Weather permitting)
  - o NOTE TO ALL RESIDENTS THAT USE SECOND AVE – EXPECT DELAYS DUE TO PAVING.
  - o NOTE TO ALL RESIDENTS THAT USE MAY AND LOOKOUT PLACE – EXPECT DELAYS AS PAVING CROSSES THESE ROADWAYS.
- SIDEWALKS / WALLS / STRIPING / SIGNING / CLEAN-UP

OVER THE NEXT TWO WEEKS.

- o EXPECT SINGLE LANE, ALTERNATING FLAGGED TRAFFIC.
- o EXPECT INTERMITTENT DETOURS AT THE INTERSECTION OF SR-20 AND SECOND AVENUE
- o TRAFFIC DELAYS ARE EXPECTED.

ADDITIONAL UPDATES WILL FOLLOW AS CONSTRUCTION CONTINUES.

CONSTRUCTION IS CURRENTLY SCHEDULED TO BE FINISHED AROUND THE MIDDLE OF OCTOBER 2008.

Thank you in advance for your cooperation and patience – Town of Twisp Public Works

Please go to [www.townoftwisp.com](http://www.townoftwisp.com) for further construction updates.
